# CENTRAL ELECTRIICTY REGULATORY COMMISSION NEW DELHI

## Petition No. 158/MP/2021 along with I.A. No. 61/2021

#### Coram:

Shri I.S. Jha, Member Shri Arun Goyal, Member Shri P.K Singh, Member

Date of Order: 01.8.2022

#### In the matter of

Petition under Sections 61, 63 and 79 of the Electricity Act, 2003 read with the statutory framework and Article 11, Article 12 and Article 16.3 of the Transmission Service Agreement dated 23.04.2019 executed between Lakadia-Vadodara Transmission Project Limited and its Long-Term Transmission Customers inter alia claiming compensation due to Change in Law events, extension to the scheduled commissioning date of the transmission project on account of the Force Majeure events adversely impacting its implementation and declaratory relief with respect to the Petitioner's scope of work.

#### And in the matter of

Lakadia-Vadodara Transmission Project Limited F-1, Mira Corporate Suites, 1 & 2, Ishwar Nagar, Mathura Road, New Delhi – 110065

....Petitioner

#### Vs

- 1. Adani Green Energy MP Limited Adani House, 4<sup>th</sup> Floor, South Wing, Shantigram, S.G. Highway, Ahmedabad – 382421
- 2. Adani Green Energy Limited Adani House, 4<sup>th</sup> Floor, South Wing, Ahmedabad – 382421
- 3. Netra Wind Private Limited B-504, Delphi Building, Orchard Avenue, Sector-5, Hiranandani Gardens, Powai, Mumbai- 400076



4. WRSS XXI (A) Transco Limited C 105, Anand Niketan, South Delhi Delhi - 110021

5. PFC Consulting Limited First Floor, Urjanidhi, 1, Barakhamba Lane, Connaught Place, New Delhi- 110001

6. Central Electricity Authority, Seva Bhawan, R.K. Puram, New Delhi- 110066

7. Central Transmission Utility of India Limited, Saudamini, Plot No.2, Sector 29, Near IFFCO Chowk, Gurgaon - 122001, India

Power Grid Corporation of India Limited
 B-9, Qutub Institutional Area,
 Katwaria Sarai,
 New Delhi – 110016

....Respondents

Parties Present: Shri Sanjay Sen, Sr. Advocate, LVTPL

Shri Deep Rao, Advocate, LVTPL

Ms. Parichita Chowdhury, Advocate, LVTPL

Ms. Harneet Kaur, Advocate, LVTPL

Shri TAN Reddy, LVTPL Shri Balaji Sivan, LVTPL Shri Gaurav Kumar, LVTPL

Shri Venkatesh, Advocate, PGCIL

Shri Ashutosh K Srivastava, Advocate, PGCIL Shri Tushar Srivastava, Advocate, PGCIL Ms. IsnainMuzamil, Advocate, PGCIL

Shri V. C. Shekhar, PGCIL Shri Prashant Kumar, PGCIL Ms. Supriya Singh, PGCIL Shri Arjun Malhotra, PGCIL

Ms. Suparna Srivastava, Advocate, CTUIL Ms. Soumay Singh, Advocate, CTUIL Shri Tushar Mathur, Advocate, CTUIL



### **ORDER**

The Petitioner, Lakadia-Vadodara Transmission Project Limited ("LVTPL") is *inter alia* claiming for compensation due to various force majeure and change in law events during the implementation of its transmission project and seeking an extension to the scheduled commercial operation date ("SCOD") of the said project in view of the delay caused by various force majeure events, in terms of Article 11 and 12 of the Transmission Service Agreement ("TSA") dated 23.04.2019.

- 2. The Petitioner also filed 61/IA/2021 after filing the instant Petition. After filing the instant petition and 61/IA/2021, the Petitioner filed 73/IA/ 2021 seeking to file amended petition and amended 61/IA/2021 which was allowed by the Commission vide Order in ROP for hearing held on 30.9.2021. Accordingly, the amended petition is considered hereon in the instant Order.
- 3. The Petitioner has made the following prayers in Petition No. 158/MP/2021:
  - a) admit and allow the present Petition;
  - b) list the present Petition for an urgent hearing;
  - hold and declare that the Petitioner was impacted by the Force Majeure events described in the Petition and is therefore, entitled to relief in accordance with Article 11 of the TSA;
  - d) hold and declare that the Project's SCOD stands extended by 8 months in terms of the MOP's Office Memorandum dated 27.07.2020 and the MOP's Letter dated 12.06.2021;
  - e) grant leave to the Petitioner to place on record additional submissions and documents for determination by this Hon'ble Commission of the actual delay caused due to the Force Majeure Events, post commissioning of the Project;

- f) direct that no Liquidated Damages may be imposed on the Petitioner for the delays caused in Project's implementation due to the aforesaid Force Majeure Events under the TSA or otherwise;
- g) grant the Petitioner appropriate Force Majeure relief in terms of Article 11 of the TSA;
- h) hold and declare that the Petitioner was impacted by the Change in Law events described in the Petition and is therefore entitled to relief in accordance with Article 12 of the TSA;
- i) grant leave to the Petitioner to place on record additional submissions and documents for determination of the actual cost impact of the Change in Law Events;
- j) grant the Petitioner appropriate Change in Law relief in terms of Article 12 of the TSA;
- k) grant the Petitioner in-principle approval in relation to prayers at (c) and (h) hereinabove as an interim measure:
- I) direct that the Petitioner is entitled to recover Interest During Construction incurred in respect of the periods of delay that were caused due to the unforeseen and uncontrollable events as described in the Petition;
- m) declare that the extra bays at Vadodara S/s do not fall within the scope of work of the Petitioner under the TSA and the scope of work for the Petitioner is limited the scope under Schedule 2 of the TSA, Article 1.2 of the RFP and the transmission license of the Petitioner:
- n) set aside the minutes of the CEA meeting held on 16.03.2021;
- o) declare that in case the Petitioner is directed to implement two extra bays at the Vadodara S/s, it shall be entitled to claim reimbursement of the additional expenditure incurred through an increase in tariff, as the said event will constitute a change in law event under Article 12 of the TSA; and
- exercise regulatory powers to grant appropriate relief to the Petitioner in the facts of this case, including by way of condoning any inadvertent errors or delays by the Petitioner, if any;
- q) pass such other order(s) and/ or direction(s) as this Hon'ble Commission may deem just and proper in the facts and circumstances of the case.
- 4. The Petitioner has made following prayers vide IA/61/2021:
  - (a) admit and allow the present Application;
  - (b) list the present Applicant for urgent hearing;

"

- (c) grant in-principle approval to the force majeure events described at Paras 38-95E of the Petition:
- (d) hold and declare that the Project's SCOD stands extended by 8 months in terms of the MOP's Office Memorandum dated 27.07.2020 and the MOP's Letter dated 12.06.2021;
- (e) grant in-principle approval to the change in law events described at Paras 99-117D of the Petition:
- (f) grant liberty to the Applicant to place on record relevant details and documents in relation to the final time and cost overrun caused due to the said force majeure and change in law events;
- (g) declare that the extra bays at Vadodara S/s do not fall within the scope of work of the Applicant under the TSA and the scope of work for the Applicant is limited to the scope under Schedule 2 of the TSA, Article 1.2 of the RFP and the transmission license of the Applicant;
- (h) In the alternative, in case the Applicant is directed to implement two extra bays at the Vadodara S/s, declare that the fresh requirement to implement the two extra bays at the Vadodara S/s is a change in law event under Article 12 of the TSA, entitling the Applicant to seek reimbursement of the additional expenditure incurred through an increase in tariff;
- (i) grant the Applicant ad interim/ ex-parte relief in terms of the prayers hereinabove; and
- (j) pass such other order(s) and/ or direction(s) as this Hon'ble Commission may deem just and proper in the facts and circumstances of the case."
- 5. The Petition was heard on 11.11.2021. The relevant extracts of RoP for hearing dated 11.11.2021 are as follows:
  - u
  - 2. The learned senior counsel for the Petitioner submitted that the present Petition has been filed, inter alia, seeking compensation due to various force majeure and change in law events occurring during the implementation of its transmission project and seeking an extension to the Scheduled Commercial Operation Date ('SCOD') of the project in view of delay caused by various force majeure events, in terms of Article 11 and Article 12 of the Transmission Service Agreement dated 23.4.2019....
  - (b) The Petitioner has filed IA No. 61/2021, inter alia, seeking in-principle approval of the various force majeure and change in law events and seeking declaration regarding scope of work of the Petitioner under the TSA.
  - (c) Regarding the scope of work, as per Clause 1.2 of the Request for Proposal (RfP) and Schedule 2 of the TSA, the Petitioner was required to implement only two 765 kV bays each at Lakadia sub-station and Vadodara sub-station for Lakadia-Vadodara 765 kV D/c transmission line. However, the Respondent, PGCIL vide its various e-mails/ letters to the

Petitioner insisted that as per the annexure to clarification on RfP and TSA dated 30.5.2019, the Petitioner is required to provide three bays in each diameter of the transmission line. The Central Electricity Authority in the minutes of the meeting held on 16.3.2021 has suggested that the implementation of the extra bays is required at Vadodara sub-station as per the provisions of the RfP.

- (d) Accordingly, the Petitioner has sought declaration as to its scope of work and in case the Petitioner is directed to implement the extra bays, it shall be entitled to claim reimbursement of the additional expenditure by way of an increased tariff, said event being a Change in Law event.
- (e) The Petitioner has sought condonation of delay under various force majeure events. In addition, the Petitioner has sought condonation of 166 days of delay on account of delay in conducting the bidding process and transfer of the Special Purpose Vehicle (Petitioner company) to the selected bidder, namely, Sterlite Grid Limited. Thus, the Commission may consider granting extension for the aforesaid period at this stage. 3. After hearing the learned senior counsel for the Petitioner, the Commission observed that since the project of the Petitioner is still under implementation and is yet to achieve the commercial operation, the consideration of the Petitioner's request for extension of SCOD on account of force majeure events at this stage may be premature as there are uncertainties regarding likely COD of the project, quantification of extension, events of force majeure (their overlapping or occurrence of new events etc.) as already noted in RoP for the hearing dated 30.9.2021.
- 4. In response, the learned senior counsel for the Petitioner submitted that while certain reliefs/ prayers regarding determination of impact of various events may be considered by the Commission only after COD of its project, the Commission may consider the prayers of the Petitioner for in-principle declaration of force majeure events and change in law events at this stage. The learned senior counsel requested that the extent to which various prayers are to be considered by the Commission in the present case may be decided by the Commission after admission of the matter.
- 5. However, for the reasons already noted above, the Commission decided to the admit the present Petition and IA only to the extent of the Petitioner's prayers relating to the inprinciple declaration of the Change in Law events and its scope of work under RfP and TSA. For the remaining prayers, the Petitioner may approach the Commission after completion of its project.
- 6. In view of the above, the Commission ordered as under:
- (a) Admit. (b) The Petitioner to serve copy of the Petition on the Respondents immediately, if not already served and the Respondents to file their reply on the prayers (h) and (m) only as detailed in the amended petition if any."
- 6. As per above, the Commission directed that since the project of the Petitioner is still under implementation and is yet to achieve the commercial operation, the consideration of the Petitioner's request for extension of SCOD on account of force majeure events at this stage may be premature as there are uncertainties regarding likely COD of the project,

quantification of extension, events of force majeure (their overlapping or occurrence of new events etc.) as already noted in RoP for the hearing dated 30.9.2021. It is observed that there is an issue raised by Petitioner with respect to scope of work. We observe that it is necessary to adjudicate the dispute regarding scope of work at this stage before COD of the project. Hence the Petition has been admitted only to the extent of the Petitioner's prayers relating to the scope of work under RfP and TSA and consequential change in Law, if any, and respondents were also directed to file their responses limited to these aspects only. Accordingly, the prayers (m) to (q) as noted at Paragraph 3 of this Order have been adjudicated upon in the instant Order. The petitioner is at liberty to file its claims under Force Majeure and Change in Law after COD of its project in accordance with law.

## **Submissions by the Petitioner**

- 7. The Petitioner has submitted as follows:
- a) The Petitioner is a special purpose vehicle ("SPV"), originally set up as a wholly owned subsidiary of PFC Consulting Limited ("PFCCL"), Respondent No. 5, with the objective of establishing the "Transmission System for WRSS-21 (Part-B) Transmission System Strengthening for relieving over loadings observed in Gujarat Intra-state system due to RE injections in Bhuj PS" ("Project") and to act as a Transmission Service Provider ("TSP") after being acquired by a successful bidder. The Petitioner is a transmission licensee under Section 14 of the Electricity Act, 2003 ("Act"). The Petitioner was granted a transmission license by the Central Electricity Regulatory Commission ("Commission") vide its Order dated 04.03.2020 in Petition No. 445/TL/2019. The Petitioner is now a wholly owned subsidiary of Sterlite Grid 18 Limited ("Sterlite").
- b) Respondent No. 1, Adani Green Energy MP Limited is the Lead Long-Term Transmission Customer ("Lead LTTC"), who is permitted to represent all the Long-Term Transmission Customers ("LTTCs") and discharge their rights and obligations.

c) MoP vide its Notification dated 01.02.2019 notified PFCCL (Respondent No. 5) as the BPC for the purpose of selection of a bidder as the TSP to establish the Project through the TBCB process. The Project consists of the following elements [*Ref: Schedule 2 of the TSA*]:

S.	Name of the Transmission Element	SCOD	
No.			
(i)	Lakadia-Vadodara 765 kV D/c line ("LV Line")	31.12.2020	
(ii)	330 MVAr switchable line reactors at both ends of Lakadia -	31.12.2020	
	Vadodara 765 kV D/c line along with 500 ohms NGR at both		
	ends of Lakadia - Vadodara 765 kV D/c line (330 MVAR line		
	reactor - 4 nos. & 765 kV Reactor bay - 4 nos.) ("Reactors")		
(iii)	2 nos. of 765 kV bays each at Lakadia and Vadodara S/s for	31.12.2020	
	Lakadia - Vadodara 765 kV D/c line (765 kV line bay - 4		
	nos.)("765 kV Bays")		

The SCOD of the Project is 31.12.2020 ("Project SCOD")

#### <u>Note</u>:

- (a) As per MoM of 3<sup>rd</sup> ECT held on 21.12.2018, it was decided that the scheme is to be implemented by December, 2020.
- (b) POWERGRID to provide space for 2 nos. of 765kV line bays and space for 2 nos. of 330MVAr switchable line reactors and reactor bays at Vadodara (GIS) for Lakadia Vadodara (GIS) 765kV D/c line.
- (c) Developer of Lakadia S/s to provide space for 2 nos. of 765kV line bays and space for 2 nos. of 330MVAr switchable line reactors and reactor bays at Lakadia for Lakadia Vadodara (GIS) 765kV D/c line.
- d) The BPC issued the Request for Qualification ("RFQ") on 17.01.2019 for shortlisting bidders and calling them for participation in the next stage of bidding i.e., Request for Proposal ("RFP"). On 18.03.2019, RFP was issued to the shortlisted bidders, including Sterlite. Pursuant to being selected as the successful bidder for the implementation of the Project, Sterlite was issued the Letter of Intent ("LOI") on 31.07.2019.
- e) The Commission vide its orders dated 04.03.2020 and 05.03.2020 in Petition No. 445/TL/2019 and Petition No. 444/AT/2019 respectively, granted the transmission license to the Petitioner and adopted the competitively discovered levelized tariff.

- f) The Petitioner has faced several uncontrollable impediments and challenges in the form of force majeure and change in law events.
- g) PGCIL, Respondent No. 8 vide its emails dated 22.10.2020 and 28.10.2020, and letters dated 12.11.2020 and 24.11.2020 to the Petitioner has insisted that while the Petitioner is planning to install 2 nos. of bays at the Vadodara S/s, as per the SLD drawing titled "Bay allocation for Vadodara GIS -Lakadia PS 765 kV D/C Line at 765 kV Vadodara GIS Substation" attached as Annex-A to the Clarifications on RFP & TSA dated 30.05.2019 ("Clarification 1"), the Petitioner is required to provide 3 Nos. bays in each diameter of the line.
- h) As per Article 1.2 of the RFP and Schedule 2 of the TSA, the Petitioner is inter alia required to implement 2 nos. of 765 kV bays each at the Lakadia S/s and Vadodara S/s for the LV Line, as part of the Project. The said provision and schedule also state that PGCIL is to provide space for 2 nos. of 765 kV line bays and space for 2 nos. of 330 MVAr switchable line reactors and reactor bays at Vadodara (GIS) for the LV Line.
- i) Annex-A to Clarification 1 relied upon by PGCIL was issued in response to the queries raised by the bidders only to indicate the bay position, and not the scope of work. Such document cannot be relied upon to add to the express scope of work of the Petitioner under the RFP and TSA. The response of the BPC to the queries at S. No. 88 and 108 of Clarification 1 clarifies the same. To confirm its understanding on the scope of work, in its queries submitted before the BPC on 02.06.2019, Sterlite asked the BPC to confirm that reference to Annex-A is to be limited for understanding the take-off gantry location and orientation, and the number of bays under the scope shall be as per the RFP only. Along with this query, a drawing marking the 2 extra nos. of bays as 'Not in Scope' was also provided to the BPC for its confirmation. However, the BPC in its Clarification dated 14.06.2019 ("Clarification 2"), at S.No. 9 reiterated that the plan layout indicating the tentative position for line bay has been provided to the bidders.

- j) On the same date i.e., 14.06.2019, the BPC has issued Amendment No. 2 to the RFP and TSA ("Amendment No. 2") amending the scope of work to also include 1 no. 110 MVAR spare reactor. However, no amendment was made to increase the number of bays to be implemented at the Vadodara S/s.
- k) The Petitioner vide its email dated 26.10.2020 informed PGCIL that the Petitioner is constructing two nos. of line bays at the Vadodara S/s, in line with the scope of work under the RFP and TSA, and that the additional scope of work mentioned by PGCIL is not within its scope of work.
- I) PGCIL vide its letter dated 12.11.2020, sought intervention of the Central Electricity Authority (CEA) to resolve the issues in relation to the scope of work of the Petitioner.
- m) In the CEA Meeting held on 16.03.2021, conducted with PGCIL, CTU, PFCCL and the Petitioner, it was deliberated if the implementation of three nos. of bays in each diameter where the D/c line would terminate is within the scope of the Petitioner. Sterlite clarified to the CEA vide its letter dated 02.04.2021 that the two extra nos. of bays at the Vadodara S/s are not within its scope of work as per the RFP and the TSA.
- n) The minutes of the CEA meeting held on 16.03.2021, that were issued on 18.06.2021, did not completely record the stand of the Petitioner on the issue of additional scope of work. Further, the CEA in the said meeting erroneously suggested that the implementation of the two extra nos. of bays is required at the Vadodara S/s as per the RFP provisions. Therefore, the Petitioner vide its letter dated 05.07.2021 to the CEA reiterated its stand on each point raised by the stakeholders involved.
- o) It was categorically pointed out that as per the scope of work under the RFP and TSA, 2 nos. of line bays are made with one Main bay & Tie bay in each diameter to comply with functional requirement of one and a half breaker switching scheme. The Petitioner pointed out that if such extra bays were required to be implemented for future use, the same should have been set out in the scope of work.

- p) In support, the Petitioner has provided examples of RFPs previously issued where if a complete diameter with future main bay was required, the same had clearly been mentioned in the scope of work. The Petitioner submitted that the Project was awarded to Sterlite on the basis of competitive bidding, and requirements that were not specified in the bidding documents cannot be made part of the TSA now.
- q) In view of the aforementioned provisions of the RFP and the TSA, and the Clarification 1 and Clarification 2 issued by the BPC, the two extra nos. of bays to be implemented at the Vadodara S/s do not fall within the scope of work of the Petitioner. The transmission license issued to the Petitioner also does not include such bays within its scope.
- r) The implementation of these two extra bays will approximately require an additional expenditure of INR 74.00 Cr. In case the Petitioner is directed to implement the said bays, the Petitioner shall stand to recover the additional cost incurred by it through an increase in tariff, by claiming the said event as a change in law event.
- s) Therefore, the Petitioner prays before the Commission to declare that the two extra nos. of bays at Vadodara S/s do not fall within the scope of the work of the Petitioner and the scope of work for the Petitioner is limited to what is stated in Schedule 2 of the TSA and Article 1.2 of the RFP. Further, in case the Petitioner is directed to implement the said bays, it shall be entitled to claim the additional expenditure through an increase in tariff as the said event will constitute a change in law event under Article 12 of the TSA.
- t) The Petitioner has intimated the LTTCs of such potential additional expenditure that may be incurred by it vide its letter dated 11.06.2021.

## Submissions by Petitioner in I.A No. 61/2021

8. Petitioner has filed amended I.A on 6.10.2021 wherein the Petitioner has reiterated its submissions made in the instant Petition and has sought in-principle approval with respect to occurrence of the said force majeure and change in law events and a declaration with respect to the scope of work of the Petitioner. Petitioner submitted that it has filed the said Application because there is an urgency to provide financial certainty on future cash flows to the lenders, in order to save the Petitioner from becoming a stressed asset.

## Submissions by Respondent No. 8, PGCIL vide affidavit dated 30.11.2021

- 9. PGCIL vide affidavit dated 30.11.2021 has submitted the following:
  - a) The scope of work under the transmission scheme WRSS 21-B, inter-alia involves implementation of associated 765 kV bays each at Lakadia and Vadodara for termination of 765 kV D/c Lakadia- Vadodara line by the Petitioner. The 765kV bays work is being implemented by LVTPL at Vadodara (GIS) substation of PGCIL.
  - b) During the implementation of the project, it was observed by PGCIL that the Petitioner was undertaking implementation of only 2 nos. bays against 3 nos. bays in each diameter of 765 kV Lakadia circuit 1 &2 at Vadodara (GIS) S/stn of PGCIL in contrast to the standard practice.
  - c) PGCIL vide its email dated 22.1.2020, 28.10.2020 and Letters dated 12.11.2020 and 24.11.2020 clarified to the Petitioner that the SLD clearly mentions that there are 3 bays in each diameter of the line and requested the Petitioner to carry out the said works at Vadodara GIS.
  - d) Despite repeated requests, the Petitioner failed to perform its obligations and issue remained unresolved and PGCIL vide its Letter dated 12.11.2020 approached CEA to intervene in the said issue. CEA upon request convened a meeting dated 16.03.2021 to deliberate over the issues raised by PGCIL with respect to scope of work associated with termination of 765kV LV line at Vadodara Substation.

e) After deliberations, with the Petitioner, PGCIL, BPC & CTUIL, CEA came to the conclusion that the Petitioner was to implement 3 Nos. against 2 No. of bays in each diameter of 765 kV Lakadia circuit 1 &2 at Vadodara (GIS) S/stn. A perusal of the minutes of meeting dated 16.03.2021 shows that the meeting conducted by CEA was a consultative process in which the Petitioner itself, amongst other stakeholders, were present. The aforesaid cannot be said to be a unilateral decision, rather after deliberations, it was agreed by all stakeholders including the petitioner that the implementation of two number of full GIS diameter comprising of 2 no. of main bays and 1 no. of tie line bay in each dia is required to be constructed by the petitioner at Vadodara GIS S/stn.

## Rejoinder to the submissions of Respondent No. 8, PGCIL

- 10. Petitioner in its rejoinder to submissions of PGCIL has submitted the following vide affidavit dated 16.12.2021:
  - Petitioner reiterated its earlier submissions regarding the scope of work of the a) Petitioner including implementation of only two number of 765 kV bays each at Lakadia S/s and Vadodara S/s for the LV Line and not required to undertake implementation of extra 2 bays at Vadodara S/s.
  - b) Sterlite Grid 18 Limited ("Sterlite") vide its letter dated 31.05.2019 to the BPC expressly sought clarification on whether the two extra bays indicated in the SLD will be a part of the scope of work. Sterlite highlighted the extra bays in the SLD as 'Not in scope' and provided a copy to the BPC for their clear reference. The BPC responded to the said query vide its Additional Clarifications dated 14.06.2019 ("Clarification 2") and inter alia stated that the plan layout of the Vadodara S/s that was provided was for indicating tentative position for line bay.
  - c) It is only recent that PGCIL has started agitating that the scope of work of the Petitioner includes two extra nos. of bays at the Vadodara S/s. As such, PGCIL is

- only an interconnecting entity and has no locus to question, interpret or decide upon the scope of work of the Petitioner.
- d) During the CEA meeting, it was inter alia mentioned by the CTU that although the scope of work under the TSA expressly mentions of only two bays at the Vadodara S/s, the requirement of implementing two extra nos. of bays was an implicit one.
- Petitioner has implemented two number of line bays at the Vadodara S/s with one e) main bay and one tie bay in each diameter to comply with the functional requirement of one and half breaker switching scheme under the RFP. Therefore, the Petitioner is in compliance with the specific technical requirement under the RFP and the concern raised during the CEA meeting stands addressed.
- f) Further, the project under implementation by the Petitioner was awarded to it post tariff based competitive bidding. The cost of implementing the two extra bays is approximately Rs. 74 crores. It cannot be argued by CEA or any stakeholder concerned including the CTU that an item requiring such heavy expenditure was an 'implicit requirement' and did not need express mentioning. The intention of the BPC is not relevant here until expressly stated. PGCIL in Para 7 of its Reply has unfoundedly argued that the Petitioner's act of proceeding with construction of only 2 nos. of bays is against the standard practice. The said argument is without any merit whatsoever and is liable to be rejected at the outset. Rather, as a matter of standard practice, whenever a complete diameter with a future main bay is required, it is clearly mentioned under the scope of work in the concerned RFP.

#### Submissions by Respondent No. 7, CTU

11. In compliance to RoP for hearing dated 11.11.2021, CTU vide affidavit dated 14.1.2022 has submitted the following:

- a) The scope of works for the Petitioner under the transmission scheme WRSS-21B inter alia involved the implementation of two numbers 765 kV bays at Vadodara S/s including the requirement of implementation of 3 nos. of bays in each dia where the D/c line would be terminated.
- b) In the Clarification on RfP & TSA for WRSS-21 (Part-B) Transmission System strengthening for relieving over loadings observed in Gujarat Intra-state system due to RE injection in Bhuj PS issued by BPC, it was clarified under Clarification No. 88. As such, the clarification as sought by the bidders was evidently with respect to the "extension works" in bay augmentation at Vadodara (GIS) wherein the scope of extension works was clarified by way of the Single Line Diagram (SLD) indicating the allocated bay at Vadodara GIS S/s. The Petitioner has wrongly contended that the SLD was only to indicate the bay position even though query pertained to the extension works as a whole and as such the Petitioner was required to proceed as per the SLD.
- c) After detailed deliberations and consideration of the views submitted by the Petitioner, PGCIL, BPC & CTUIL, in the meeting dated 16.3.2021, it was agreed that the implementation of two number of full GIS dia comprising of 2 no. of main bays and 1 no of tie line bay is required at Vadodara GIS S/stn as per the RfP provisions. Non-adherence by M/s LVTPL would tantamount to non-compliance of the bidding documents by M/s LVTPL.

## Rejoinder to the submissions of Respondent No. 7, CTU

- 12. Petitioner vide reply dated 20.1.2022 has reiterated its earlier submissions, however additional information in response to the reply of CTU is as follows:
  - a) During the CEA meeting dated 16.3.2021, it was inter alia mentioned by the CTU that although the scope of work under the TSA expressly mentions of only two bays at the Vadodara S/s, the requirement of implementing two extra nos. of bays was an implicit one. The arguments raised by CTU, PGCIL, BPC and CEA during

the said meeting are denied and the Petitioner does not agree with the conclusion reached by the CEA.

- b) Petitioner has implemented two number of line bays at the Vadodara S/s with one main bay and one tie bay in each diameter to comply with the functional requirement of one and half breaker switching scheme under the RFP. Therefore, the Petitioner is in compliance with the specific technical requirement under the RFP and the concern raised during the CEA Meeting stands addressed.
- c) As per the provisions of RFP and TSA, clarifications 1 and 2 issued by the BPC, the two extra nos. of bays to be implemented at the Vadodara S/s do not fall within the scope of work of the Petitioner. The transmission license issued to the Petitioner also does not include such bays within its scope of work.

### Hearing dated 24.1.2022

- 13. Petitioner, PGCIL and CTU made detailed submissions in the matter on the aspect of the 'scope of the work' under the TSA and RfP documents reiterating their submissions made in the petition.
- 14. After hearing the parties, the Commission observed that despite notice, none was present on behalf of the BPC, PFCCL. The Commission expressed its displeasure over casual approach of BPC.
- 15. Commission sought certain information from the Petitioner, PGCIL and PFCCL and reserved the order in the matter.

## **Submissions by PGCIL**

16. In compliance of RoP for hearing dated 24.1.2022, PGCIL vide affidavit dated 11.2.2022 has submitted the following additional information:

- a) As per Annexure A attached with the Additional Clarifications of the RFP document there are 3 Nos. bays in each DIA of the line that were supposed to be implemented by the Petitioner.
- b) In the RfP document under Specific Technical Requirements for S/stn, at para 2 of Clause 2.3 (765 kV GIS S/stn equipment), it is clearly stated that "the arrangement of gas sections or compartments shall be such as to facilitate future extension of any make without any drilling, cutting or welding on the existing equipment. To add equipment, it shall not be necessary to move or dislocate the existing switchgear bays."
- c) Under Specific Technical Requirements for the S/stn (in the RfP), it is mentioned that One and half breaker switching scheme has to be considered at 765 kV switchyard with each ckt of D/c line to be terminated in different diameter.
- d) From the SLD and General Layout of Vadodara GIS S/stn attached with the clarifications issued by the BPC, it is clear that the 2nd main bay in each dia would be utilized for future augmentation.
- e) Gas Insulated Substation (GIS) being a compact in their design, the land requirement is significantly reduced in GIS in comparison to Air Insulated Substation (AIS). The techno-commercial consideration requires to implement future requirements of assets at inception stage. Since GIS is a sophisticated and modular technology, implementation of complete diameter with future bays has been envisaged at the very beginning as part of planning to comply with one and half breaker scheme for connectivity with both the main buses.
- f) In the Clarification no. 88 on RfP & TSA issued by BPC, it is evident that the clarification sought by the bidders was with respect to the "extension works" in bay augmentation at Vadodara (GIS) wherein the scope of extension works was clarified by way of the Single Line Diagram (SLD) titled "Bay Allocation for Vadodara GIS-Lakadia PS 765 kV D/C Line at 765 kV Vadodara GIS Substation"

indicating the allocated bay at Vadodara GIS S/s. Thus, as per the RfP LVTL is required to implement 3 nos. bays in each diameter of 765 kV Lakadia circuit 1 &2 at Vadodara (GIS) S/stn.

## Submissions by Respondent No. 5, PFCCL

- 17. In compliance to RoP for hearing dated 24.1.2022, PFCCL vide affidavit dated 18.2.2022 has submitted the following additional information:
  - (a) As per the definitions provided in RFP document, "RFP" shall mean this Request for Proposal document along with all schedules, annexures and RFP Project Documents attached hereto and shall include any modifications, amendments, alterations or clarifications thereto.
  - (b) On 18.03.2019, RFP documents were issued to eight (08) RFQ qualified bidders including Sterlite Grid 18 Limited based on the project specific details provided by CTU vide their letter dated 15.02.2019.
  - (c) A pre-bid conference was held on 15.04.2019 to address the queries of the Bidders. The bidders had also submitted their queries on the RFP documents to the BPC.
  - (d) The queries raised by the Bidders pertaining to the technical inputs provided by CTU were forwarded to CTU and CEA for providing clarifications. On receipt of clarifications from CTU and confirmation/clarifications from CEA, the clarifications to the queries were issued to the bidders.
  - (e) The clarifications after being confirmed from CEA were issued to the bidders vide letter dated 30.05.2019. The clarifications related to bay extension works at Vadodara S/s are reiterated such as Sr. no. 6, 7, 11, 15, 16, 88, 92, 100, 108, 109 and 110. Along with the clarifications a layout of the Vadodara S/s indicating the scope of the bay extension works at Vadodara S/S was shared with the bidders. According to the layout submitted, the complete bay extension works is within the scope of the TSP.

- (f) Petitioner vide letter dated 31.05.2019 submitted the additional queries regarding bay extension works at Vadodara S/s against the clarifications issued earlier indicating that 2 extra bays as indicated in the layout of the Vadodara S/s is not in the scope of the TSP by marking the same as "Not In Scope" in the drawing attached thereto. The additional queries raised by the bidders along with the aforementioned query were forwarded to CTU/CEA vide mail dated 11.06.2019 and 13.06.2019 for clarifications and confirmation from their end. The consolidated additional clarification and proposed amendments to RFP documents were submitted to CEA vide mail dated 13.06.2019. CEA vide mail dated 13.06.2019 confirmed the clarifications and advised to issue the same to the bidders. The additional clarifications after being confirmed from CEA were issued to the bidders vide letter dated 14.06.2019. The clarification to the aforementioned query raised by the Petitioner was already clarified vide clarifications dated 30.5.2019 and is reiterated.
- (g) The reply clarifies that the implementation of 765 kV bays at Vadodara S/S termination of 765 kV D/c Lakadia-Vadodara line was in the scope of the TSP.
- (h) The query pertaining to the additional 2 no. of bays for bay extension works was sought by the Petitioner only and no other bidder raised the query regarding the aforementioned issue. The BPC vide their clarification at S. No. 6, 7,110 issued to all the bidders on 30.05.2019 has made it clear that the scope of work indicated in the drawing was within the scope of TSP.
- (i) Even after the issuance of the additional clarifications, the bidders including Petitioner had substantial amount of time to raise further queries regarding any ambiguity on the scope of bay extension work. However, no queries were raised by any bidder including Petitioner which further establishes the fact that all the bidders including Petitioner had agreed to the scope of the bay extension works at the Vadodara S/s as clarified by the BPC.
- (j) The issues related to the implementation of bays at Vadodara S/s were addressed by CEA in the meeting dated 16.3.2021 and after a consultative process, the

Petitioner, amongst the other stakeholders agreed that the implementation of two number of full GIS dia comprising of 2 no. of main bays and 1 no of tie line bay is to be constructed by the Petitioner at Vadodara S/s as indicated in the scope of bay extension works in the drawing issued by the BPC.

- (k) As is evident from the RFP document, the clarifications issued to the queries and the MoM dated 18.06.2021 above and submissions herein, it is clear that the implementation of the bay extension works as mentioned in the RFP and layout of the Vadodara S/s were within the Scope of the TSP.
- (I) CEA had revised the scope of work and accordingly, an amendment (Amendment No. 2) to the RFP documents was issued to the bidders on 14.06.2019.

## **Submissions by Petitioner**

- 18. In compliance to RoP for hearing dated 24.1.2022, Petitioner vide affidavit dated 5.3.2022 has submitted the following additional information:
  - (a) The specific technical requirements for substations prescribed under the clause 1.2 of RFP inter alia state that one and half breaker scheme arrangement is required to be followed for the 765 kV bays under implementation by the Petitioner. It is submitted that the bay design and switching scheme implemented by the Petitioner is in line with the said technical requirement.
  - (b) PGCIL has placed reliance on the SLD of the Vadodara S/s attached as Annex-A to the Clarifications on the RFP and TSA issued by the BPC on 30.05.2019 (i.e., Clarification 1) to claim that the Petitioner was required to implement three number of bays at the Vadodara S/s. The said SLD was provided for reference of the bidders in response to Query Nos. 88 and 108 and only in context of tentative position and orientation of bays.
  - (c) Sterlite vide its letter dated 31.05.2019 to the BPC (emailed on 02.06.2019) sought clarification on whether the two extra bays indicated in the SLD will be a

part of the scope of work. Sterlite highlighted the extra bays in the SLD as 'Not in scope' and provided a copy to the BPC for their clear reference. The BPC responded to the said query vide its Additional Clarifications dated 14.06.2019 (i.e., Clarification 2) and inter alia stated that the plan layout of the Vadodara S/s that was provided was for indicating tentative position for line bay.

- (d) The aforesaid Clarification 2 was issued by the BPC on 14.06.2019 and on the same date, BPC issued an Amendment to the RFP and TSA to inter alia add one switchable line reactor (spare unit) at the Vadodara end to the scope of work of the successful bidder. However, no change whatsoever was made to the number of bays to be implemented by the successful bidder.
- (e) In case of the Petitioner, its scope of work was to construct two 765 kV line bays at Vadodara S/s in a one and half breaker scheme. Since the LV line is a double circuit line, each circuit was to be terminated in a different diameter (as stated in the RFP). Nowhere does the RFP or TSA specify that three circuit breakers and two feeders are to be implemented in the form of a full diameter. The half diameter, one and half breaker scheme so implemented by the Petitioner meets the full scope of work, functionality and reliability of the one and half breaker arrangement as the feeder would still be getting power even in case of outage of any one of the buses or circuit breakers.
- (f) The reason a half diameter was constructed was because the RFP did not ask for provision of any additional feeders in the scheme. As stated above, in the past and even in some recent bids, wherever space for future extension of bays has been envisaged, the same has been clearly mentioned along with a provision for full diameter.
- (g) The Petitioner seeks to rely on the Manual on Substations ("Manual"), prepared by Central Board of Irrigation and Power ("CBIP"), which is commonly relied upon by power utilities, manufacturers, and the engineering fraternity for guidance on

implementation of substations. It captures the industry-wide understanding on prudent utility practices on various aspects of implementation of substations. The term 'Prudent Utility Practices' has been defined under Clause 1.1.1 of the TSA to inter alia mean practices, methods and standards that are generally accepted internationally from time to time by electric transmission utilities for the purpose of ensuring the safe, efficient and economic design, construction and commissioning of the Project. Petitioner has implemented the two bays at the Vadodara S/s as per prudent utility practices as required under Clause 4.1(b)(ii) of the TSA

- (h) As per the Manual, the switching scheme for 765 kV level in GIS has to be one and half breaker scheme or a double bus scheme, as also required under Clause 1.2 of the RFP. Volume 3 of the Manual provides a list of drawings detailing the typical layouts for substations including 765 kV GIS substation such as the Vadodara S/s. Drawing No. 8.8(a) is an SLD with One and half breaker scheme at 765 kV level and double main bus scheme at 400 kV level implemented at the Koteshwar S/s by PGCIL. The one and half breaker scheme arrangement implemented by PGCIL has been outlined in a red cloud for ease of reference of the Commission. PGCIL has suppressed and obfuscated this from the record in its Reply dated 30.11.2021. It is pertinent to note that the manner in which the Petitioner has implemented one and half breaker switching scheme at Vadodara S/s is identical to the manner in which PGCIL itself has implemented the same scheme at the Koteshwar S/s.
- (i) BPC has stated that the additional queries raised by the bidders were forwarded to the CTU/CEA for confirmation at their end, and the CEA vide its email dated 13.06.2019 confirmed the clarifications and advised that they may be issued to the bidders. It is submitted that the said submission is false. It appears that the CEA did not confirm the draft clarification prepared by the BPC with respect to query no. 9 raised by the bidders. The copy of the CEA's email dated 13.06.2019 where the CEA has clearly stated in reference to Query 9 raised by the Petitioner that the said clarification may be issued after receipt of confirmation from the

CTU/PGCIL. However, no email or correspondence from the CTU/PGCIL confirming the said response has been placed on record by the BPC. It appears that without having received any confirmation from the CTU, the BPC issued the said clarifications in a reckless manner, without any regard whatsoever to the bidders' investment of time and cost.

- (j) It is also clear from the said email that the CEA was not clear about the scope of additional bays and therefore, it suggested to the BPC to seek clarity from the CTU. Contrary to the said evidence, in its minutes dated 16.03.2021, it has been suggested that the implementation of the additional bay is an implicit requirement.
- (k) The BPC has stated that even after the issuance of Clarification 2, the Petitioner had sufficient time to raise further queries, but no queries were raised by it. In response, it is submitted that after Clarification 2 was issued by the BPC on 14.06.2019, Sterlite had raised another follow up query vide its letter dated 19.06.2019 to the BPC. Vide the said letter, the Petitioner expressly asked if the additional bays were within its scope of work. The SLD of the substation, marking the additional bays as 'Not in Scope' was also attached for the reference of the BPC. However, it received no response whatsoever from the BPC on it.

## **Analysis and Decision**

19. We have considered the submissions of Petitioners and Respondents. The following issue arises for our consideration:

Whether the Petitioner is required to implement 3 breakers for each diameter at Vadodara Substation under the Scope of work as per Article 1.2 of the RFP, Schedule 2 of the TSA and the transmission license of the Petitioner?

The above issue is being dealt in the succeeding paragraphs.

- 20. The Petitioner has submitted that as per the provisions of RFP and TSA, clarifications 1 and 2 issued by the BPC, the two extra nos. of bays as directed to be implemented vide CEA meeting dated 16.3.2022, at the Vadodara S/s do not fall within the scope of work of the Petitioner. The transmission license issued to the Petitioner also does not include such bays within its scope of work. Further, in case the Petitioner is directed to implement the said bays, it shall be entitled to claim the additional expenditure through an increase in tariff as the said event will constitute a change in law event under Article 12 of the TSA.
- 21. PGCIL vide its email dated 22.1.2020, 28.10.2020 and Letters dated 12.11.2020 and 24.11.2020 clarified to the Petitioner that the SLD clearly mentions that there are 3 bays in each diameter of the line and requested the Petitioner to carry out the said works at Vadodara GIS.
- 22. PGCIL submitted that CEA conducted a meeting on 16.3.2021 with PGCIL, CTU, PFCCL and the Petitioner to deliberate the issues with respect to scope of work associated with termination of 765kV Lakadia-Vadodara line at Vadodara Substation, wherein it was discussed that the Petitioner was required to implement 3 Nos. bays in each diameter of 765 kV Lakadia circuit 1 & 2 at Vadodara (GIS) S/stn. Petitioner submitted that the said minutes did not completely record the stand of the Petitioner on the issue of additional scope of work.
- 23. The Bid Process Coordinator, PFC submitted that as per the definitions provided in RFP document, "RFP" shall mean this Request for Proposal document along with all schedules, annexures and RFP Project Documents attached hereto and shall include any modifications, amendments, alterations or clarifications thereto. The queries raised by the

Bidders pertaining to the technical inputs provided by CTU were forwarded to CTU and CEA for providing clarifications. On receipt of clarifications from CTU and confirmation/clarifications from CEA, the clarifications to the queries were issued to the bidders.

- 24. We have considered the submissions of Petitioner and Respondents. Let us examine the scope of works for Petitioner as per various documents on record.
- 25. Detailed Scope of Work as per Article1.2 of RFP and Schedule 2 of TSA are as follows:

S.	Name of the Transmission Element	SCOD
No.		
(i)	Lakadia–Vadodara 765kV D/c line ("LV Line")	31.12.2020
(ii)	330MVAr switchable line reactors at both ends of Lakadia – Vadodara 765kV D/c line along with 500 ohms NGR at both ends of Lakadia – Vadodara 765kV D/c line (330 MVAR line reactor - 4 nos. &765kV Reactor bay - 4 nos.) ("Reactors")	31.12.2020
(iii)	2 nos. of 765kV bays each at Lakadia and Vadodara S/s for Lakadia – Vadodara 765kV D/c line (765kV line bay - 4 nos.) ("765 kV Bays")	31.12.2020

## Note:


26. Clarification No. 1 dated 30.5.2019 issued by PFC provides as follows:

<sup>(</sup>a) As per MoM of 3<sup>rd</sup> ECT held on 21.12.2018, it was decided that the scheme is to be implemented by December, 2020.

<sup>(</sup>b) POWERGRID to provide space for 2 nos. of 765kV line bays and space for 2 nos. of 330MVAr switchable line reactors and reactor bays at Vadodara (GIS) for Lakadia – Vadodara (GIS) 765kV D/c line.


<sup>(</sup>c) Developer of Lakadia S/s to provide space for 2 nos. of 765kV line bays and space for 2 nos. of 330MVAr switchable line reactors and reactor bays at Lakadia for Lakadia – Vadodara (GIS) 765kV D/c line."

S. No.	Clause No. and Existing provision	Clarification Required	Clarifications
		BPC to confirm above.	
88.	Extn. Sub-station	Kindly provide following details for extension works in bay augmentation at Vadodara (GIS) —  a. SLD. b. Overall General Electrical Layout. c. Outdoor Cable Trench Layout. d. 765KV GIS Hall Drawing. e. Make of Existing SAS equipment f. Make of Existing 76KV GIS equipment g. 765KV GIS Bus Bar Extension Module along with GIS Bus Adopter detail. h. Availability of auxiliary supply (AC-DC) i. Availability of space in CRB/ CRP Roon in GIS hall. j. Earthing Layout. k. Make and Type of bus bar Protection l. Availability of optical port in FOTE equipment. Also confirm if TSP is liable for any kind of payment to existing substation owner for access to their facilities during construction & Operations phase.	SLD and GA indicating the allocated bay at Vadodara GIS S/S is attached.     Make of existing GIS is M/s NHVS, China     Make of Existing SAS is M/s Siemens     Regarding other details, as sought, bidder may visit the substation and acquaint themselves with the existing provisions.  TSP shall coordinate with existing substation owner regarding access to the existing facilities during construction and operation phase.
10	8. RfP Technical	Vadodara GIS - 765 kV Bay Extn 2 Nos.765 kV line take off Bay orientation not indicated in RfP document	The plan layout of Vadodara GIS substation (PGCIL) indicating the tentative position for line bay is attached at Annex-A.

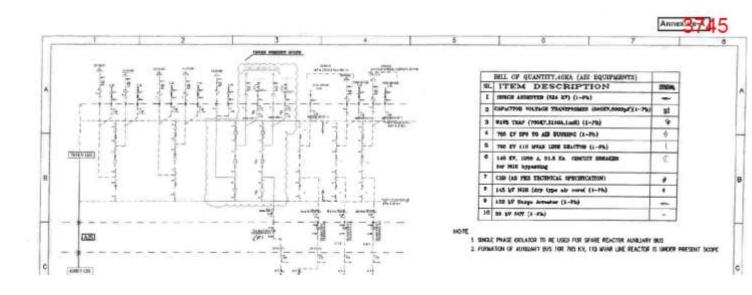

27. Vide Clarification No. 2 BPC, clarified as follows:

S. No.	Clause No. and Existing Provision	Clarification Sought by Bidder	Clarifications
9.	Sr No. 108 / RfP Technical  Clarifications on RFP & TSA for WRSS-21 (Part-B) - Transmission System strengthening for relieving over loadings observed in Gujarat Intra-state system due to RE injections in Bhuj PS Dated: 30/05/2019  ANNEXURE - A / Drawing No: C/ENGG- SS/TBCB/WRSS-21B/VADODARA/SLD/01 REV_00 and: C/ENGG-SS/TBCB/WRSS- 21B/VADODARA	As per the response received, "Annexure-A drawings need to be referred for Bay allocation at 765KV Vadodara GIS station." However, we presume that the Take-off gantry location and Orientation shall be referred from Drawing No: "C/ENGG-SS/TBCB/WRSS-21B/VADODARA" and number of Bays under present scope shall be as per RFP only and the extra two (2) no 765KV Bays other than RFP requirement, shown in drawing: C/ENGG-SS/TBCB/WRSS-21B/VADODARA/SLD/01 REV_00 shall not be in present scope of work as shown in enclosed drawing "Annexure 1" marked as "NOT IN SCOPE"	The plan layout of Vadodara GIS substation (PGCIL) indicating the tentative position for line bay was already provided to the bidders. However, the bidders are advised to coordinate with substation owner for exact termination at Vadodara end.



28. The transmission license issued to the Petitioner, pursuant to Order dated 4.3.2020 in Petition No. 445/TL/2019, provides the following elements:

## SCHEDULE

Project Related Details:

The project comprises of the following elements of the inter-State Transmission System:

S.No.	Name of the Transmission Element	Schedule date of Commissioning
1.	Lakadia-Vadodara 765 kV D/c line	
2.	330 MVAr switchable line reactors at both ends of Lakadia-Vadodara 765 kV D/c line along with 500 ohms NGR at both ends of Lakadia-Vadodara 765 kV D/c line (330 MVAr line reactor-4 nos., 765 kV Reactor bay-4 nos., 1x110 MVAr 765 kV, 1 ph. Switchable line reactor (spare unit ) at Vadodara end)	31 December, 2020
3.	2 nos. of 765 kV bays each at Lakadia and Vadodara S/s for Lakadia-Vadodara 765 kV D/c line (765 kV line bay-4 nos.)	

Licence No. 63/Transmission/2020/CERC
Authority: Orders of the Commission dated 23.1.2020 and 4.3.2020 in Petition No. 445/TL/2019.

- 29. As per the above apart from line reactor bays, only 2 nos. of 765kV bays at Vadodara S/s for Lakadia Vadodara 765kV D/c line has been provided for.
- 30. The issue under dispute in regards to scope of works associated with termination of 765 kV Lakadia-Vadodra D/C line at Vadodra(PG) S/S was deliberated in a meeting organised by CEA on 16.03.2021 wherein PGCIL, CTU, PFCCL including the Petitioner were present. The relevant extracts of the minutes are as follows:

"Issue no. 1: Inadequate no. of bays being implemented by M/s LVTPL in each diameter at Vadodara (GIS) S/stn of PGCIL, wherein 765kV Lakadia Ckt1 and Ckt2 would be terminated.

Discussions held:

1. Powergrid:

- 1.1 The Specific Technical Requirements for Substation works mentioned in the RfP document of the scheme specified that the developer needs to implement one and half breaker switchig scheme for 765 kV switchyard and each circuit of a double circit line shall be terminated in different diameter. Further the SLD for the Vadodara GIS S/stn was provided by Powergrid as an Annexure to the 'Additional Clarification on RfP' sought by the bidders. In the SLD (attached as Annexure A), it was clearly highlighted that the scope of works under the scheme included implemented of 3 nos. of bays in each dia where the D/c line would be terminated.
- 1.2 The intention behind inclusion of implementation of the second main bay in each dia is that in case of a GIS substation, installation of bay in a half equipped GIS diameter at a later date becomes non-feasible. However, it is observed M/s Sterlite is undertaking implementation of only 2 nos. CBs against 3 nos. CBs in each dia of 765 kV Lakadia Ckt1 and Ckt2 at Vadodara (GIS) S/stn of PGCIL. This is not in compliance to what was envisaged in the RfP documents issued to bidders and would result in non-optimal utilisation of space at Vadodara (GIS) S/stn.

#### 2. *M/s LVTPL*:

- 2.1 The RFP issued by PFC Consulting Ltd on 18/03/2019 defines the scope of work as "2 nos of 765 kV bays each at Lakadia and Vadodara S/s for Lakadia Vadodara 765 kV D/c line (765 kV line bay-4 nos.)" With reference to this RFP, bidders asked for existing station drawings & line take off bay orientations. In response of those queries, BPC (PFC Consulting Ltd) issued clarification on 30.05.2019. Vide sl. No-88 & 108 of this clarification, BPC shared Vadodara station related drawing in Annexure –A as reference for indicating the bay position only, not as scope of work.
- 2.2. Further to the clarification pertaining to line take off bay orientation, M/s LVTPL submitted additional queries BPC on 31/05/2019, especially marking the 2 nos. extra bays in Annexure-A and seeking the clarification that these extra 2 nos bays shall not be in the scope of work of the present scheme..
- 2.3. In response to this additional query, the clarification provided by BPC on 14/06/2019 at sl. No. 9 was that the plan layout indicating tentative position was already provided to the bidders. So, it is very much clear from this RFP that queries were noted by the authority & the issued drawing is only tentative bay position only.
- 2.4. Further on the same date (14/06/2019) BPC issued the amendment for scope of works for the scheme, wherein increase of 1 no. 110 MVAR spare Reactor was clearly mentioned as scope Amendment. However, there was no amendment for nos. of bays at Vadodara GIS station and it remained same as original RFP scope of work i.e 2 Nos. 765kV Line Bays at Vadodara
- 2.5. In view of the above-mentioned points, it is clear that the implementation of 2 Nos. line bays with switchable line Reactor bays at Vadodara GIS substation by M/s LVTPL is in line with RfP scope of work & its subsequent amendments.

#### 3. BPC (PFCCL):

- 3.1 The scope of works incorporated in the RfP document did not specify the description of CBs to be installed in each diameter at the S/Stn, it was clarified that One and half breaker switching scheme has to be considered at 765 kV switchyard with each ckt of D/c line to be terminated in different diameter. Further, in response to the query raised by the bidder with respect to SLD and General Electric layout for extension works in bay augmentation at Vadodara, PFCCL in its clarification dated 30/05/2019 at S. No. 88 attached the SLD and General Arrangement indicating the allocated bay at Vadodara GIS S/S. In the attached SLD, the detailed arrangement of each dia and the scope of works under the present scheme was clearly highlighted.
- 3.2 Also, since the same SLD was to be referred in response to the query regarding 765 kV take-off bay orientation, BPC in its clarification at S. No. 108 provided to refer to the same SLD for the plan layout of Vadodara GIS substation (PGCIL) indicating the tentative position for line bay.

- 3.3 Accordingly, it was intended that the same SLD needs to be referred for the bay extension works to be carried out at Vadodara GIS S/stn as well as for the tentative position for line bay. Therefore, the contention of M/s LVTPL that the SLD enclosed was to be used as reference for indicating the bay position only and not as scope of work is not correct.
- 3.4 Further, M/s LVTPL has stated that it raised additional query pertaining to line take off bay orientation wherein it sought clarification regarding 2 extra no bays in each dia. In this regard, it may be mentioned that as no drawing highlighting the bays under question from the bidder was received. Accordingly, in the clarification furnished by BPC, the general reply to refer to the already provided plan layout of Vadodara GIS S/stn was given. Based on the general reply, M/s LVTPL seems to have presumed that the 2<sup>nd</sup> main bay in each dia may be done away with instead of seeking further clarification.

#### 4. *CTU*:

- 4.1 As mentioned in RfP document, M/s LVTPL has to implement One and half breaker switching scheme at Vadodara GIS S/stn and each ckt of Lakadia-Vadodara D/c line has to be terminated in two separate diameters. In case of AIS, half dia can be constructed and the 2<sup>nd</sup> main bay can be constructed at a later time for the future feeders. However, in case of GIS, it is prudent to construct the complete full diameter at one go as future interfacing is difficult. The same has been deliberated in RPC(TP)s of Western Region and Northern Region, wherein it was decided that in case of GIS sitchyard, full diameter needs to be implemented from the beginning itself even though the second bay would be utlised in future.
- Also, as far as M/s LVTPL's submission of strictly adhering with the scope of works as mentioned in RfP document is concerned, it may be mentioned that in the scope, only two no. of bays at Vadodara GIS S/stn was explicitly mentioned. However, in adherence to the implicit requirements of implementation of One and half breaker switching scheme, M/s LVTPL is implementing tie bays ineach diameter. Nowhere in the RfP document, implementation of tie bays was explicitly mentioned. So, provision of one and half breaker scheme with full dia in the RfP itself, implies that two main and tie bay has to be implemented in each dia. Explicit mentioning of details of numbers of bays in each diamater in the scope of works in the RfP document is not a common practice. However, when the bidder coordinates with existing S/stn owner with regard to augmentation works to be carried out, these things also gets clarified. Further, the two nos. 765 kV bays of each dia has been marked for termination of Ahmedabad-Vadodara 765 kV D/c line at Vadodara substation.

#### 5. CEA

5.1 In the RfP document under Specific Technical Requirements for S/stn, at para 2 of Clause 2.3 (765 kV GIS S/stn equipment), it is clearly stated that 'the arrangement of gas sections or compartments shall be such as to facilitate future extension of any make without any drilling, cutting or welding on the existing equipment. To add equipment, it shall not be necessary to move or dislocate the existing switchgear bays'.


Under Specific Technical Requirements for the S/stn (in the RfP), it is metioned that One and half breaker switching scheme has to be considered at 765 kV switchyard with each ckt of D/c line to be terminated in different diameter.

From the SLD and General Layout of Vadodara GIS S/stn attached with the clarifications issued by the BPC, it is clear that the 2<sup>nd</sup> main bay in each dia would be utilised for future augmentation. In view of above, if M/s LVTPL is not undertaking implementation of 2<sup>nd</sup> main bay ineach dia at Vadodara GIS S/s, then it would not be able to comply with the above mentioned clauses of the RfP document.

After detailed deliberations, it ws agreed that the implementation of twonumber of full GIS dia comprising of 2 no. of main bays and 1 no of tie line bay is required at Vadodara GIS S/stn as per the RfP provisions. Non-adherence of M/s LVTPL would tantamount to non-compliance of the bidding documents by M/s LVTPL."

We observe that the RFP as well as license provides for 2 no. 765kV bays at Vadodra associated with Lakadia- Vadodra transmission line. However, subsequent to RFP vide Clarification No. 1 dated 30.5.2019, an SLD was attached with Clarification where 3 breakers were indicated against each diameter. However, we observe that vide Clarification No. 88 where SLD is provided for does not refer to Annexure-A which is referred to at Clarification No. 108 where Annexure-A is provided for "take off gantry bay orientation".

31. Petitioner has submitted that vide its letter dated 31.05.2019 to the BPC (emailed on 02.06.2019), and expressly sought clarification on whether the two extra bays indicated in the SLD will be a part of the scope of work. Petitioner has submitted that it highlighted the extra bays in the SLD as 'Not in scope' and provided a copy to the BPC for their clear reference.

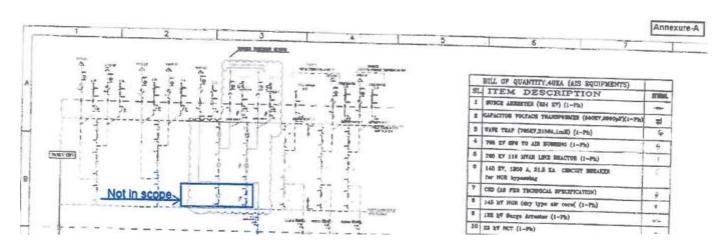

Petitioner queried as follows:

"As per the response received, "Annexure-A drawings need to be referred for Bay allocation at 765KV Vadodara GIS station." However, we presume that the Take-off gantry location and Orientation shall be referred from Drawing No: "C/ENGG- SS/TBCB/WRSS-21B/VADODARA" and number of Bays under present scope shall be as per RFP only and the extra two (2) no 765KV Bays other than RFP requirement, shown in drawing: C/ENGG-SS/TBCB/WRSS-21B/VADODARA/SLD/01 REV\_00 shall not be in present scope of work as shown in enclosed drawing "Annexure 1" marked as "NOT IN SCOPE"

To the above BPC clarified as follows:

"The plan layout of Vadodara GIS substation (PGCIL) indicating the tentative position for line bay was already provided to the bidders. However, the bidders are advised to coordinate with substation owner for exact termination at Vadodara end."

The snapshot of Clarification No. 2 issued by BPC, is as follows:

S. No.	Clause No. and Existing Provision	Clarification Sought by Bidder	Clarifications
9.	Sr No. 108 / RfP Technical  Clarifications on RFP & TSA for WRSS-21 (Part-B) - Transmission System strengthening for relieving over loadings observed in Gujarat Intra-state system due to RE injections in Bhuj PS Dated: 30/05/2019  ANNEXURE - A / Drawing No: C/ENGG- SS/TBCB/WRSS-21B/VADODARA/SLD/01 REV_00 and: C/ENGG-SS/TBCB/WRSS- 21B/VADODARA	As per the response received, "Annexure-A drawings need to be referred for Bay allocation at 765KV Vadodara GIS station." However, we presume that the Take-off gantry location and Orientation shall be referred from Drawing No: "C/ENGG-SS/TBCB/WRSS-21B/VADODARA" and number of Bays under present scope shall be as per RFP only and the extra two (2) no 765KV Bays other than RFP requirement, shown in drawing: C/ENGG-SS/TBCB/WRSS-21B/VADODARA/SLD/01 REV_00 shall not be in present scope of work as shown in enclosed drawing "Annexure 1" marked as "NOT IN SCOPE"	The plan layout of Vadodara GIS substation (PGCIL) indicating the tentative position for line bay was already provided to the bidders. However, the bidders are advised to coordinate with substation owner for exact termination at Vadodara end.

- 32. We observe that BPC vide the above said clarification did not reply anything on the aspect of "NOT IN SCOPE" and rather limited its reply on the first part of query related to "take off gantry". We also observe that on 14.06.2019, the BPC has issued Amendment No. 2 to the RFP and TSA ("Amendment No. 2") amending the scope of work to also include 1 no. 110 MVAR spare reactor. However, no amendment was made to clarify the scope of work including implementation of complete diameters with 3 breakers in each diameter at the Vadodara S/s.
- 33. We note that PFCCL vide meeting held at CEA on 16.3.2021 stated as follows:

"In this regard, it may be mentioned that as no drawing highlighting the bays under question from the bidder was received. Accordingly, in the clarification furnished by BPC, the general reply to refer to the already provided plan layout of Vadodara GIS S/stn was given. Based on the general reply, M/s LVTPL seems to have presumed that the 2nd main bay in each dia may be done away with instead of seeking further clarification."

As per above, PFCCL representative attending the meeting at CEA on 16.3.2021 stated that they have not received any drawing from Petitioner.

- 34. Commission vide ROP for hearing held on 24.1.2022 asked Respondent, PFCCL to clarify as follows:
- "4...
  c)Respondent, PFCCL to clarify regarding its reply with respect to query of the Petitioner dated 31.5.2019 towards bays shown as "NOT IN SCOPE" (i.e. at Sr.9 of Additional Clarifications of RfP& TSA Queries). Whether the reply clarifies the position as to whether such bays shown as "NOT IN SCOPE" are to be implemented or not to be implemented?"
- 35. In regards to above said query, PFCCL vide Affidavit dated 18.2.2022 has acknowledged receipt of query dated 31.5.2019 by Petitioner along with drawing thereto. PFCCL has further submitted that it forwarded the query to CEA and CTU and issued clarifications as approved by CEA and CTU.
- 36. BPC has been assigned responsibility of carrying out the bidding process for which it is duly compensated for. BPC must be very careful while issuing clarifications, when it is aware that clarifications form part of RFP. Here following casualness is noted on part of BPC, PFCCL
  - a. The scope of work is the starting point of bidding. There should be no ambiguity in scope of work. In the bidding document of the scheme, 2 nos. of 765 kV bays at

Vadodara substation has been specified. If it was known upfront that full diameter has

to be constructed in GIS, the same should have been clearly provided in RFP.

b. BPC nowhere indicated SLD is at Annexure-A and the same is specifying scope of

work as per clarifications dated 30.5.2019.

c. Further at one point of time during meeting held on 16.3.2021, PFCCL is refusing

receipt of Drawing at Annexure-1 of petitioner's guery dated 31.5.2019 and while filing

affidavit at Commission, it acknowledged receipt of the same. This clearly implies that it

did not see the drawing at the time of issuing the clarification no. 2. Even vide its reply

in instant petition, rather than taking the responsibility of error on its part on ignoring

the drawing, it has tried to pass on the blame on to CTU and CEA. Even if BPC is

taking support of CEA or CTU, finally before issuing clarifications, it is the responsibility

of BPC to ensure completeness of query and its reply.

37. Let us peruse the relevant clause regarding the switching scheme as mentioned in

RFP.

38. The RFP provides as follows:

"SPECIFIC TECHNICAL REQUIREMENTS FOR SUBSTATION

1.0.....

1.1....

1.2 Switching Scheme

It is essential that the system should remain secure even under conditions of major equipment or bus-bar failure. Substations being the main connection points have large influence on the security of the system as a whole. The selection of the bus switching scheme is governed by the various technical and other related factors. One & Half breaker bus scheme for 765kV has been generally considered due to its merits in terms of reliability, security, operational

flexibility and ease of maintenance of equipment. At 765kV switchyard, each circuit of a double circuit line shall be terminated in different diameter.

.....

It is observed that RFP mandates that in 765 kV switchyard each circuit of a double circuit line shall be terminated in different diameter. However, at the same time RFP nowhere mandates "one and a half breaker" scheme, rather the RFP suggests to consider ""one and a half breaker scheme" citing its advantages. In case anything is a mandate, it should be clearly provided for in the document, rather than including it as an option.

#### 39. Further Clause 2.3 of the RFP is as follows

## Service continuity requirement for GIS:

## "2.3 765KV GIS Substation equipment

40. In regard to above, petitioner has submitted that the entirety of Clause 2.3 has to be looked into rather than a particular portion of the clause. The entire clause is extracted hereinbelow:

#### "2.3 765KV GIS Substation equipment

GIS (Gas Insulated Switchgear) shall be indoor type and in accordance to IEC: 62271-203. The switchgear shall be designed and specified to withstand operating conditions and duty requirements. All the switchgear such as Circuit Breaker, isolator, earth switch including CT, PT etc. shall be GIS type. Surge Arrestors used for transformer/Reactor connections will be AIS or GIS type. 765kV scheme shall be designed in such a way that it shall be possible to use line reactors (if provided) as bus reactors, in case of outage of line, to control bus voltage. Local control cabinets

(LCC) shall be provided as per requirement. The alarm & annunciation of GIS equipment shall be wired to SCADA System.

The GIS assembly shall consist of separate modular compartments e.g. Circuit Breaker compartment, Bus bar compartment filled with SF6 Gas and separated by gas tight partitions so as to minimize risk to human life, allow ease of maintenance and limit the effects of gas leaks failures & internal arcs etc. These compartments shall be such that maintenance on one feeder may be performed without de-energizing the adjacent feeders. These compartments shall be designed to minimize the risk of damage to adjacent sections and protection of personnel in the event of a failure occurring within the compartments. Rupture diaphragms with suitable deflectors shall be provided to prevent uncontrolled bursting pressures developing within the enclosures under worst operating conditions, thus providing controlled pressure relief in the affected compartment. The arrangement of gas sections or compartments shall be such as to facilitate future extension of any make without any drilling, cutting or welding on the existing equipment. To add equipment, it shall not be necessary to move or dislocate the existing switchgear bays. As the GIS is likely to be extended in future the TSP shall make available the complete details for the design of interface module such as cross section, enclosure material, enclosure dimensions (inner & outer), Flange diameter (inner & outer), conductor cross-section & connection arrangement, bolt spacing & dimension, rated gas pressure, Gasket detail etc. Further, adequate space for GIS Busbar Interface module shall be taken into account for future scope.

The material and thickness of the enclosures shall be such as to withstand an internal flash over without burns through for a period of 300 ms at rated short time withstand current. The material shall be such that it has no effect of environment as well as from the by-products of SF6 breakdown under arcing condition. This shall be validated with Type Test.

Each section shall have plug- in or easily removable connection pieces to allow for easy replacement of any component with the minimum of disturbance to the remainder of the equipment. Inspection windows (View Ports) shall be provided for Disconnect Switch and both type of earth switches i.e., Maintenance and fast operating.

#### Service continuity requirement for GIS:


The GIS equipment with the given bus switching arrangement is divided into different gas compartments. During the work such as a fault repair or major maintenance, requiring the dismantling of a gas compartment for which more than one compartments may need to be degassed.

During the above following Service continuity conditions shall be ensured to the extent possible:


- •For One & half breaker bus switching scheme, during a fault in Circuit Breaker compartment, no bus bar and feeder is permitted out of service during maintenance and repair/replacement.
- •For Double Main bus switching scheme, during a fault in Circuit Breaker compartment, no bus bar is permitted out of service during maintenance and repair/replacement.
- •During a fault in GIS compartment other than Circuit Breaker compartment, maximum one bus bar and/or one feeder is permitted out of service during maintenance and repair/replacement."
- 41. Petitioner has submitted that it is clear from a bare perusal of the said clause that it refers to expansion of the GIS by using bus interface modules and requires space to be left

for the same and that the GIS shall be extended from the main bus and the said requirement has been complied with by the Petitioner. The Petitioner has further contended that the said clause does not require implementation of additional bays by the Petitioner. It has submitted that the GIS shall be extended from the Main Bus in the same way LVTPL is extending the existing PGCIL GIS without any drilling, cutting or welding on the existing equipment.

42. Petitioner has also submitted example of Koteswar substation of PGCIL where 765kV GIS has been implemented in manner as been implemented by the Petitioner at Vadodara. A snapshot of SLD of Vadodara GIS S/s as submitted by Petitioner vide affidavit dated 27.11.2021 is as follows:

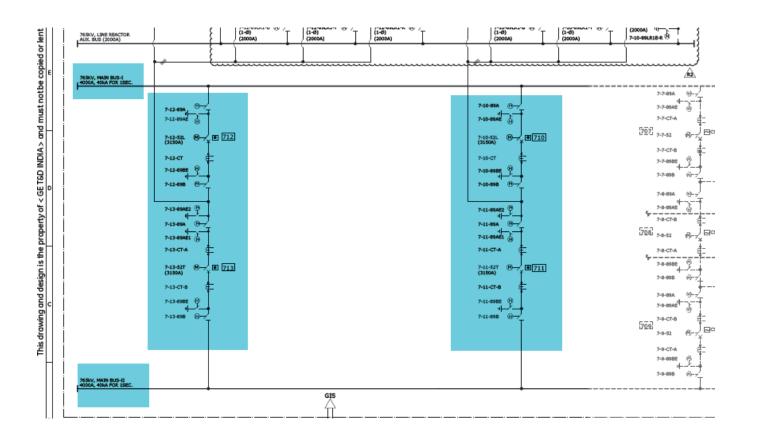

A snapshot of SLD of Koteshwar GIS S/s of Powergrid as submitted by Petitioner vide affidavit dated 27.11.2021 is as follows:

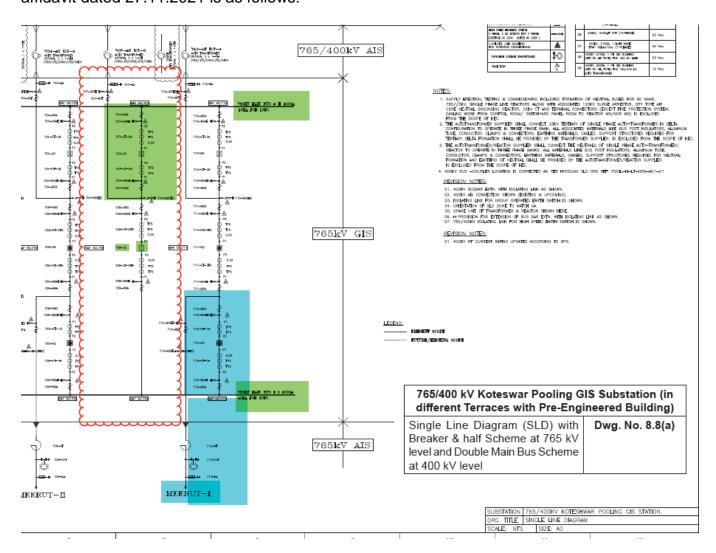

From the above SLD it can be seen that there are diameters at Koteshwar which have 3 breakers and diameter with two breakers also. The petitioner has also implemented 2 breakers for each diameter. Hence, it is observed that it is not a technical mandate to construct 3 breakers for each diameter. Rather, it would depend on the scheme of things as planned. We observe that Clause 2.3 of RFP as quoted at paragraph 40 above provides under "service continuity requirement of GIS" options of "one and a half breaker scheme" or "double main scheme". The scheme implemented by Petitioner is actually double main

double breaker scheme which was an option under the RFP. We have already observed at paragraph 38 that "one and half breaker scheme" was only an option to be considered by petitioner.

43. Petitioner has also attached a few RFPs issued subsequent to instant RFP, where the RFP has been modified to remove the ambiguities. One such RFP in case of Khavda dated 28.01.2022 issued by REC Transmission Projects Company Limited provides as follows:

#### B.1.2 Switching Scheme

The switching schemes, as mentioned below, shall be adopted at various voltage levels of substation/switchyard:

Substation	765kV side	400kV side	220kV side (Future)
765/400/220kV Khavda	One & half	One & half	Double Main
PS-2 (KPS2) (GIS) S/s	breaker (GIS)	breaker (GIS)	(GIS)

#### Notes: -

- At 765kV & 400kV voltage level, each circuit of a double circuit transmission line shall be terminated in different diameters.
- ii) Transformers and bus reactors of same HV rating shall be placed in different diameters (i.e. two transformers of same HV rating shall not be connected in the same diameter and similarly two bus reactors of same HV rating shall also not be connected in the same diameter).
- iii) In case of GIS substation where the bus scheme is One & Half breaker scheme, the diameters (diameter is a set of 3 circuit breakers with associated isolators, earth switches, current transformers etc. for controlling of 2 numbers feeders) shall be complete with feeder/line side isolator to be used for any future line with switchable line reactor bay and GIS duct of the future bay shall be brought outside the GIS hall/building with extension/interface module suitably.

We observe that in the abovesaid RFP, it has been clearly provided that requirement is for one and a half breaker scheme (3 breakers in each diameter along with associated isolators, earth switches, current transformers etc. for controlling 2 numbers feeders) and the diameters shall be complete with feeder/ line side isolator for future expansion. However, in the instant case, the same was not specified.

- 44. Hence as per the foregoing discussions, we observe that the 765kV GIS bays for Lakadia-Vadodra line at Vadodra being implemented by the petitioner are in accordance with RFP and it is not required to implement the third breaker for each diameter as per the RFP. Accordingly, prayers (m) to (q) of the Petition and (g) to (j) of IA 61/2021 are resolved. With respect to other prayers of the Petition and IA 61/2021, the same shall be as observed at Paragraph 6 of the Order.
- 45. We direct that, Vadodara substation being an important substation, the Petitioner must ensure compliance to Clause 2.3 of the RFP, for future expansions. It is further directed that BPC and CTU should make scope of work very clear without any ambiguity for projects under TBCB and take utmost care while issuing clarifications.
- 46. Petition No. 158/MP/2021 along with 61/IA/2021 is disposed of in terms of the above.

Sd/ Sd/ Sd/
(P.K. Singh) (Arun Goyal) (I.S. Jha)
Member Member Member
